



Residential apartment, Tower-final QA and handover snag list

Job Reference: US-F033-NYC
Start Date: 06/15/2025



Auditor Name: Jason Patel
Auditor Company Name: Urban QA services LLC



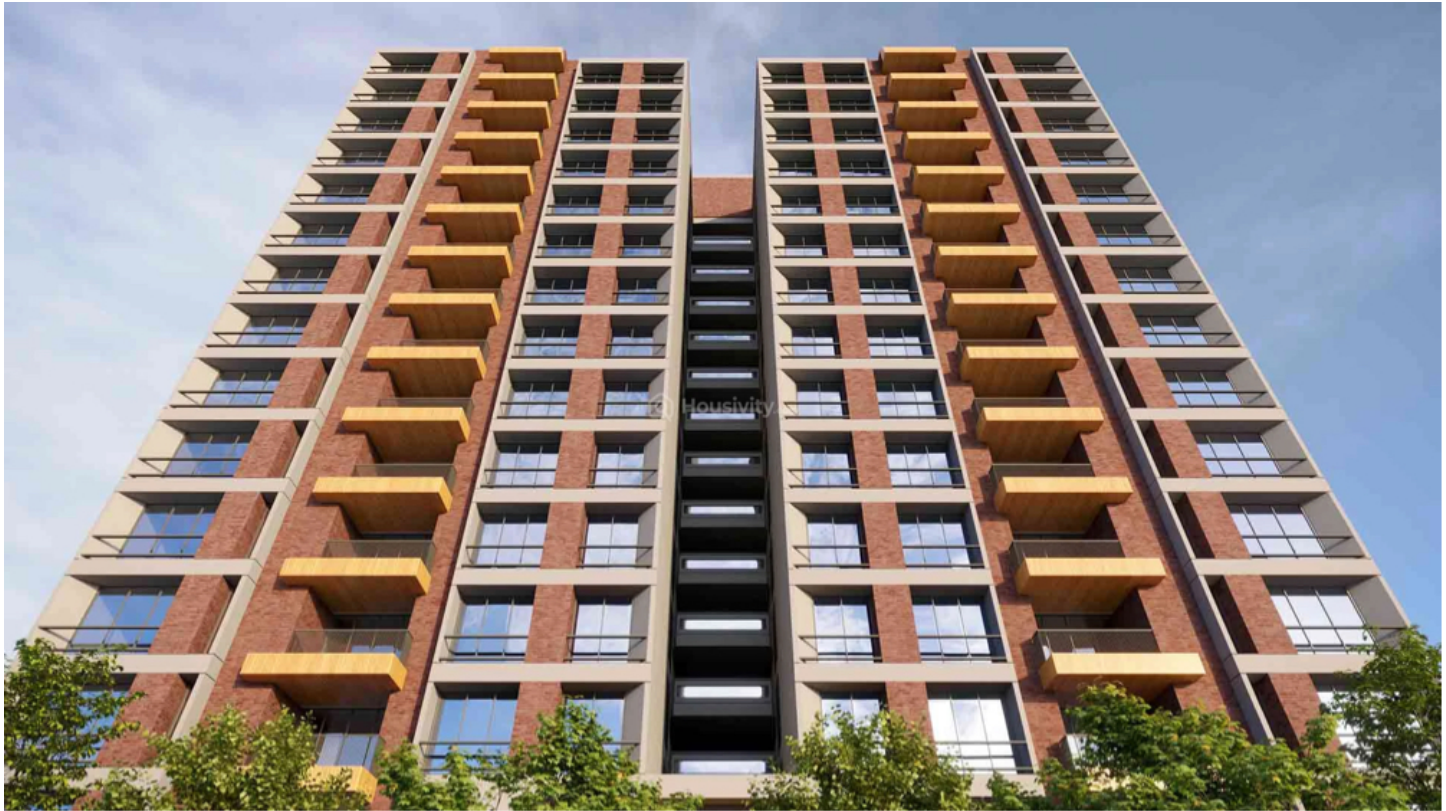

Project:	Residential apartment, Tower-final QA and handover snag list	Client Name:	Emily Rodriguez
Job Reference:	US-F033-NYC	Company Name:	Skyline real estate holdings
Start Date:	06/15/2025	Auditor Name:	Jason Patel
Location:	845 8th Avenue, New York NY 10019, USA	Auditor Company Name:	Urban QA services LLC
Total Snags:	10		

Wardrobe Handle Loose and Wobbling

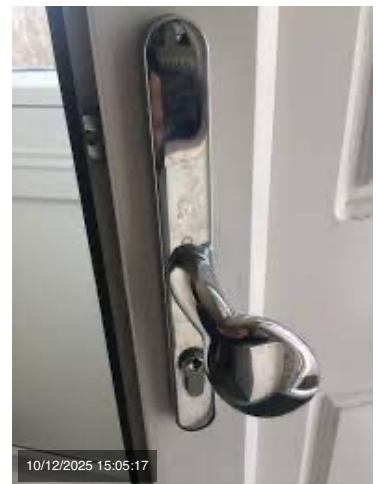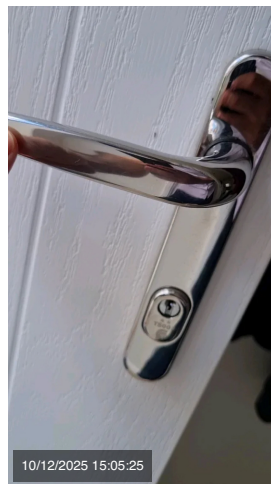


Fixed By Date: 10/30/2025
Priority: Medium
Status: Testing
Tag: Windows & Doors
Assign To: K Ryan-carpenter team

Description

The metal handle on wardrobe door is loose, causing improper grip. Tighten screws or replace hardware to match existing finish.

Ceiling Patch Marks Visible After Repair

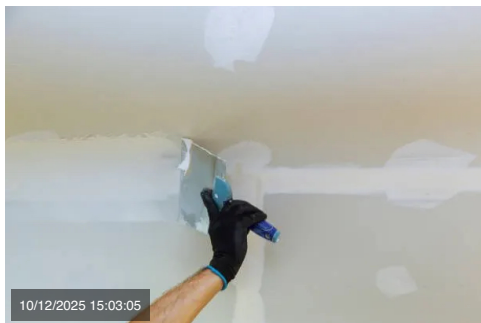



Fixed By Date: 10/30/2025
Priority: Medium
Status: In Progress
Tag: Finishing
Date Raised: 10/01/2025
Assign To: Painter team
Description

The false ceiling shows patchy texture where repair work was carried out. Needs surface sanding and uniform repainting for a smooth finish.

Bedroom Window Glass Scratched








Fixed By Date: 10/29/2025
Priority: Major
Status: Pending
Tag: Windows & Doors
Date Raised: 10/02/2025
Assign To: Paul Anderson

Description

Sliding glass panel has visible scratches affecting clarity. Replace the damaged panel and verify frame alignment after installation.

Missing Skirting Board in Living Room

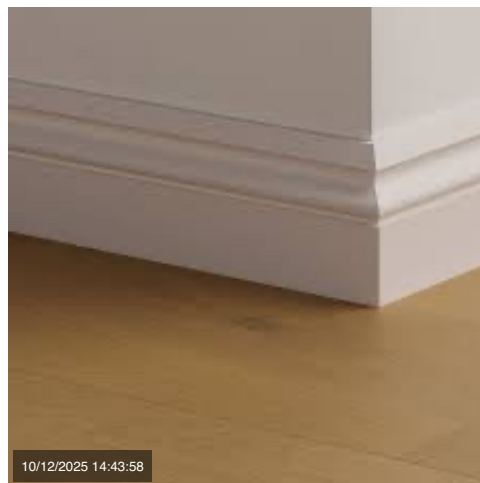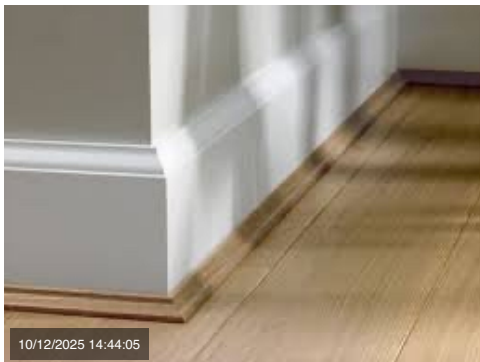

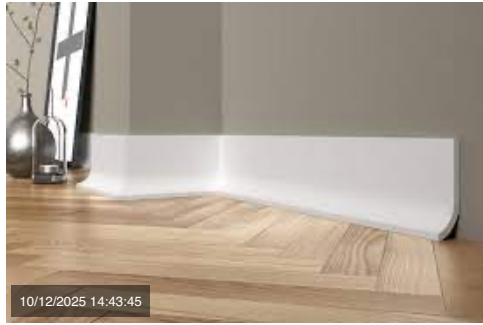

Fixed By Date: 10/31/2025

Priority: Blocker

Status: On Hold

Tag: Flooring

Date Raised: 10/02/2025

Assign To: Call Anderson

Description

Skirting strip missing along the wall behind sofa placement. Needs installation of matching finish skirting and proper adhesive fixing

Balcony Railing Found Loose





Fixed By Date: 10/31/2025
Priority: Medium
Status: Duplicate
Tag: Structural
Date Raised: 10/02/2025
Assign To: Fabrication team-Linda

Description

Balcony railing slightly shakes when leaned on. Base anchoring bolts need tightening and rust protection coating. Safety check mandatory before handover.

Water Leakage Behind Bathroom Wall






Fixed By Date: 10/29/2025
Priority: Urgent
Status: Reopened
Tag: Plumbing
Date Raised: 10/17/2025
Assign To: Plumber-Jack Ryan

Description

Damp patch observed behind WC area. Suspected leakage from concealed plumbing line. Wall needs inspection, rectification, and retiling after repair.

Electrical switch not working

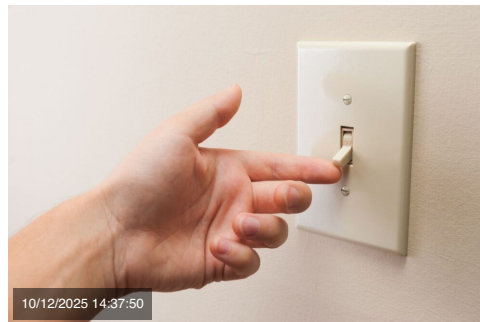

Fixed By Date: 10/29/2025
Priority: Immediate Action
Status: In Progress

Tag: Electrical
Date Raised: 10/09/2025
Assign To: Electrician

Description

Bedroom switch for ceiling light is non-operational. Possible wiring fault behind switchboard. Requires continuity test and replacement of switch if defective.

Cracked Floor Tile Near Kitchen Entry



Fixed By Date: 10/31/2025
Priority: Medium
Status: Open
Tag: Flooring
Date Raised: 10/10/2025
Assign To: Flooring contractor

Description

One ceramic tile at the kitchen threshold is cracked, likely due to impact during installation. Tile must be replaced and grout color matched.

Main Door Not Aligned Properly



Fixed By Date: 10/15/2025
 Priority: Medium
 Status: Open
 Tag: Windows & Doors
 Date Raised: 10/10/2025
 Assign To: Carpenter Anil Agarwal

Description

The main door rubs against the frame and does not latch smoothly. Hinges appear loose and need realignment. Replace rubber beading if required.

Wall Paint Peeling Near Window Frame



Fixed By Date: 10/15/2025
Priority: Major
Status: Open
Tag: Painting
Date Raised: 10/10/2025
Assign To: Painter team

Description

The emulsion paint is peeling off near the living room window, exposing the primer surface. Possible moisture seepage from outer wall detected. Needs repaint and waterproofing check.
